

# Mulberry at City Park Sewer Line Replacement

Hello! You'll receive this communication every two weeks as Utilities work takes place in the City Park area. Project managers from Utilities, Streets and our contractor, Connell Resources, will be on site daily so feel free to flag them down!

After 13 weeks, the project remains on schedule, and now is in the final phase. Traffic control and the roadway closure of Mulberry between Shields and Taft is still in place. Utilities and Streets continue to work together to manage adjustments to traffic control and road closures to maintain safety for crews and the traveling public. Crews continue to work at the west end of the project between Cook Street and Crestmore Drive and will work toward the west.

CONSTRUCTION SCHEDULE		MAR	APR	MAY	JUNE	JULY	AUG
PHASE 1	Traffic Control/Setup	█					
	Manholes & Sewer Line	█	█	█			
	Waterline		█	█			
	Service Connections			█	█		
	Temporary Road Surface			█			
PHASE 2	Traffic Control/Setup				█		
	Install Sewer & Manholes				█	█	
	Install New Services					█	
	Repair Concrete					█	
	Connect Services						█
	Replace Asphalt			█	█		█
	Landscape Repairs						█

## PROGRESS TO DATE

- All excavation trenches are backfilled and preparing for new asphalt pavement
- Completed all 17 residential service lines along West Mulberry


**THE PROJECT REMAINS ON SCHEDULE.**

**See map on back for ongoing traffic pattern.**

## WHAT TO EXPECT NEXT

- Local business access continues to City Park Plaza, City Park Pool, Golf and Fire Station from Shields Street on Mulberry – Taft Hill Road local access is still CLOSED
- Asphalt patching continues heading west in the 1800 block of W. Mulberry between Cook and Crestmore
- Full overlay surfacing of W. Mulberry from Cook Street to Taft Hill Road will begin
- Residential landscaping is being repaired
- Traffic control adjustments will continue and access will be maintained

# Traffic Pattern Remains in Effect

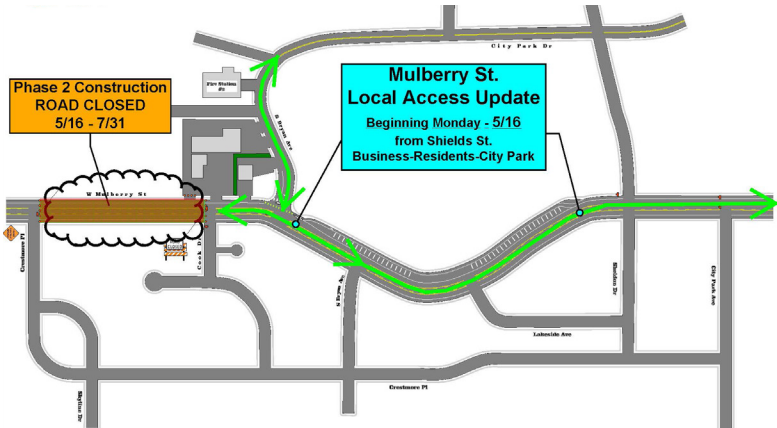

*Crews removed an old brick sewer manhole*

*Repairing landscape after sewer service installation*

*Connecting sewer service in backyard*

**NOTICE** - The Streets Department will continue overlay surfacing on Mulberry west to Overland Trail following completion of the Utilities project.

## WHO TO CALL and WHERE TO LOOK

**Jason Stutzman**, Utilities Project Manager  
970-221-6212 or [jstutzman@fcgov.com](mailto:jstutzman@fcgov.com)

**Bill Welborn**, Streets Project Manager  
970-581-5900 or [bwelborn@fcgov.com](mailto:bwelborn@fcgov.com)

## VISIT THESE WEBSITES FOR MORE PROJECT INFORMATION

- [fcgov.com/Mulberry-Sewer](http://fcgov.com/Mulberry-Sewer) for periodic updates on the Utilities project and to sign up for email updates
- [fcgov.com/mulberry2022](http://fcgov.com/mulberry2022) for updates to the Mulberry Corridor Improvements



Auxiliary aids and services are available for persons with disabilities. V/TDD: 711  
Esta información puede ser traducida, sin costo para usted, 970-212-2900.
